


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	Project duration	228 days	Mon 10/23/06	Wed 9/5/07		
2	Mobilize	7 days	Mon 10/23/06	Tue 10/31/06		Kiwi Newton
3	Structure	105 days	Wed 11/1/06	Tue 3/27/07		
4	Foundations and Fill	23 days	Wed 11/1/06	Fri 12/1/06		
5	excavate and place trench footings	10 days	Wed 11/1/06	Tue 11/14/06	2	Kiwi Newton
6	block for foundations	9 days	Wed 11/8/06	Mon 11/20/06	5FS-5 days	Neivex Masonry
7	back fill foundations	8 days	Thu 11/16/06	Mon 11/27/06	6FS-3 days	Kiwi Newton
8	Site services	15 days	Mon 11/13/06	Fri 12/1/06		Kiwi Newton
9						
10	Masonry Ground floor	27 days	Tue 11/28/06	Wed 1/3/07		
11	Gridline 1 to 6, E to K	8 days	Tue 11/28/06	Thu 12/7/06	7	Neivex Masonry
12	Gridline 1 to 10, A to D	5 days	Fri 12/8/06	Thu 12/14/06	11	Neivex Masonry
13	Gridline 1 to 10, L to P	5 days	Fri 12/15/06	Thu 12/21/06	12	Neivex Masonry
14	Gym area	4 days	Fri 12/22/06	Wed 12/27/06	13	Neivex Masonry
15	Gridline 10 to 11, D to L	5 days	Thu 12/28/06	Wed 1/3/07	14	Neivex Masonry
16						
17	Floor Structure	29 days	Fri 12/8/06	Wed 1/17/07		
18	Structural Steel second floor framing	22 days	Fri 12/8/06	Mon 1/8/07	11	Shanon
19	Precast	4 days	Tue 1/9/07	Fri 1/12/07	18	Coreslab
20	Precast topping	3 days	Mon 1/15/07	Wed 1/17/07	19	Kiwi Newton
21						
22	Masonry Second floor	25 days	Thu 1/18/07	Wed 2/21/07		
23	Gridline 1 to 6, E to K	8 days	Thu 1/18/07	Mon 1/29/07	20	Neivex Masonry
24	Gridline 1 to 10, A to D	6 days	Tue 1/30/07	Tue 2/6/07	23	Neivex Masonry
25	Gridline 1 to 10, L to P	6 days	Wed 2/7/07	Wed 2/14/07	24	Neivex Masonry
26	Gym area	5 days	Thu 2/15/07	Wed 2/21/07	25	Neivex Masonry
27						
28	Roof Structure	32 days	Mon 2/12/07	Tue 3/27/07		
29	Structural Steel roof framing	8 days	Mon 2/12/07	Wed 2/21/07	26FS-8 days	Shannon
30	Steel Deck	8 days	Thu 2/22/07	Mon 3/5/07	29	Shannon
31	Parapet blocking	5 days	Fri 3/2/07	Thu 3/8/07	30FS-2 days	Kiwi Newton
32	roofing	13 days	Fri 3/9/07	Tue 3/27/07	31	Pollard Enterprises
33						
34	Interior work	205 days	Thu 11/23/06	Wed 9/5/07		
35	Ground floor	176 days	Thu 11/23/06	Thu 7/26/07		
36	under ground M&E outside of gridline 1 to 6, E to K	10 days	Thu 11/23/06	Wed 12/6/06	7FS-3 days	CEC Mechanical, Fortis Electric
37	place SOG granular outside of gridline 1 to 6, E to K	4 days	Tue 12/5/06	Fri 12/8/06	36FS-2 days	Kiwi Newton
38	SOG outside of gridline 1 to 6, E to K	3 days	Thu 12/7/06	Mon 12/11/06	37FS-2 days	Kiwi Newton
39	under ground M&E inside of gridline 1 to 6, E to K	5 days	Fri 12/8/06	Thu 12/14/06	11	CEC Mechanical, Fortis Electric
40	place SOG granular inside of gridline 1 to 6, E to K	3 days	Fri 12/15/06	Tue 12/19/06	39	Kiwi Newton
41	SOG inside of gridline 1 to 6, E to K	3 days	Wed 12/20/06	Fri 12/22/06	40	Kiwi Newton
42						
43	M&E, sprinkler distribution and rough in under second floor	40 days	Thu 1/11/07	Wed 3/7/07	19FS-2 days	CEC Mechanical, Fortis Electric
44	HVAC distribution	25 days	Thu 2/15/07	Wed 3/21/07	43FS-15 days	CEC Mechanical
45	scrape walls ready for primer	5 days	Thu 3/22/07	Wed 3/28/07	44	JVH Masonry
46	misc. blocking and patching	5 days	Thu 3/29/07	Wed 4/4/07	45	Kiwi Newton
47	Prime paint and first coat paint	10 days	Wed 3/28/07	Tue 4/10/07	32	Interior Illusion
48	Drywall at office areas including ceilings	15 days	Wed 3/28/07	Tue 4/17/07	32	Canaan
49	T bar ceiling grid	15 days	Fri 3/30/07	Thu 4/19/07	47FS-8 days	Canaan
50	HVAC drops and diffusers	15 days	Fri 4/6/07	Thu 4/26/07	49FS-10 days	CEC Mechanical
51	Electrical fixtures and devices (ceilings)	20 days	Fri 4/6/07	Thu 5/3/07	49FS-10 days	CEC Services
52	Millwork and lockers	15 days	Fri 5/4/07	Thu 5/24/07	51	Second Generation, Gene
53	Flooring	25 days	Fri 5/11/07	Thu 6/14/07	52FS-10 days	Accord, Zet Master
54	Hang doors	15 days	Fri 6/1/07	Thu 6/21/07	53FS-10 days	Kiwi Newton
55	Plumbing fixtures	10 days	Fri 6/1/07	Thu 6/14/07	52FS-10 days, 53F	CEC Mechanical
56	Final paint	10 days	Fri 6/15/07	Thu 6/28/07	55	Interior Illusion
57	Washroom partitions, she	10 days	Fri 6/29/07	Thu 7/12/07	56	WG Wood



Task Name	Duration	Start	Finish	Predecessors	Resource Names	10/15	10/22	10/29	11/5	11/12	11/19	11/26	December	12/3	12/10	12/17	12/24	January	12/31	1/7	1/14	1/21	1/28	February	2/4	2/11	2/18	2/25	March	3/4	3/11	
misc. finishes	10 days	Fri 7/13/07	Thu 7/26/07	57	All																											
<b>Second floor</b>	<b>132 days</b>	<b>Tue 3/6/07</b>	<b>Wed 9/5/07</b>																													
M&E, sprinkler distributio	40 days	Tue 3/6/07	Mon 4/30/07	30	CEC Services,CEC Mec																											
HVAC distribution	25 days	Tue 4/10/07	Mon 5/14/07	61FS-15 days	CEC Mechanical																											
scrape walls ready for pri	5 days	Tue 5/15/07	Mon 5/21/07	62	JVH Masonry																											
misc. blocking and patchi	5 days	Tue 5/22/07	Mon 5/28/07	63	Kiwi Newton																											
Prime paint and first coat paint	10 days	Tue 5/22/07	Mon 6/4/07	47,63,32	Interior Illusion																											
Drywall at office areas including ceilings	15 days	Tue 5/22/07	Mon 6/11/07	32,47,63	Canaan																											
T bar ceiling grid	15 days	Thu 5/24/07	Wed 6/13/07	65FS-8 days,49	Canaan																											
HVAC drops and diffuser	15 days	Thu 5/31/07	Wed 6/20/07	67FS-10 days,50	CEC Mechanical																											
Electrical fixtures and dei	20 days	Thu 5/31/07	Wed 6/27/07	67FS-10 days,51	CEC Services																											
Millwork and lockers	15 days	Thu 6/28/07	Wed 7/18/07	69,52	Second Generation,Gen																											
Flooring	25 days	Thu 7/5/07	Wed 8/8/07	70FS-10 days,53	Accord,Zet Master																											
Hang doors	15 days	Thu 7/26/07	Wed 8/15/07	71FS-10 days	Kiwi Newton																											
Plumbing fixtures	10 days	Thu 7/26/07	Wed 8/8/07	71FS-10 days,70F	CEC Mechanical																											
Final paint	10 days	Thu 8/9/07	Wed 8/22/07	73,55	Interior Illusion																											
Washroom partitions, shelving	5 days	Thu 8/23/07	Wed 8/29/07	74,56	WG Wood																											
misc. finishes	5 days	Thu 8/30/07	Wed 9/5/07	75	All																											
<b>Gym - to be used as storage area during construction</b>	<b>111 days</b>	<b>Wed 3/28/07</b>	<b>Wed 8/29/07</b>																													
Paint ceiling and walls	3 days	Wed 3/28/07	Fri 3/30/07	32	Interior Illusion																											
Electrical rough in	5 days	Mon 4/2/07	Fri 4/6/07	79	CEC Services																											
HVAC hang units and duct work, hang fans etc.	7 days	Mon 4/9/07	Tue 4/17/07	80	CEC Mechanical																											
Electrical finishes at ceiling	3 days	Wed 4/18/07	Fri 4/20/07	81	CEC Services																											
Area open for storage	0 days	Fri 4/20/07	Fri 4/20/07	82																												
Area closed for storage	0 days	Wed 8/8/07	Wed 8/8/07	71,53																												
Gym equipment	5 days	Thu 8/9/07	Wed 8/15/07	84	Sheridan,Patry																											
Flooring	5 days	Thu 8/16/07	Wed 8/22/07	85	Accord,Zet Master																											
Final finishes and paint touch ups	5 days	Thu 8/23/07	Wed 8/29/07	86	All																											
<b>Mechanical room</b>	<b>48 days</b>	<b>Thu 1/25/07</b>	<b>Mon 4/2/07</b>																													
Pour and place housekeeping pads	3 days	Thu 1/25/07	Tue 1/30/07	91SF	Kiwi Newton																											
Crane large in equipment (keep covered)	2 days	Tue 1/30/07	Wed 1/31/07	23	CEC Mechanical,CEC Services																											
Steel structure above roofing	2 days	Mon 2/12/07	Tue 2/13/07	26FS-8 days	Mirage steel																											
Paint primer and first finish	2 days	Fri 2/16/07	Mon 2/19/07	93	Interior Illusion																											
Mechanical work	20 days	Tue 2/20/07	Mon 3/19/07	94	CEC Mechanical																											
Electrical hook ups	10 days	Tue 3/20/07	Mon 4/2/07	95	CEC Services																											
<b>Exterior Building</b>	<b>73 days</b>	<b>Fri 12/15/06</b>	<b>Tue 3/27/07</b>																													
Windows Ground Floor	10 days	Fri 12/15/06	Thu 12/28/06	13FS-5 days	Aerloc																											
Brick, Spray foam ground floor	20 days	Fri 12/29/06	Thu 1/25/07	99	JVH Masonry																											
Windows second floor	10 days	Mon 2/5/07	Fri 2/16/07	25FS-8 days	Aerloc																											
Brick, Spray foam second floor	20 days	Wed 2/7/07	Tue 3/6/07	100,101FS-8 days	JVH Masonry																											
Brick, Spray foam mechanical	10 days	Wed 3/7/07	Tue 3/20/07	102	JVH Masonry																											
Louvers	5 days	Wed 3/21/07	Tue 3/27/07	103	CEC Mechanical																											
<b>Exterior Site</b>	<b>144 days</b>	<b>Mon 12/4/06</b>	<b>Thu 6/21/07</b>																													
Site grading outside of building	5 days	Mon 12/4/06	Fri 12/8/06	8	Kiwi Newton																											
paving B gravel	5 days	Mon 12/11/06	Fri 12/15/06	107	Wesley																											
curbs and walks	15 days	Mon 4/23/07	Fri 5/11/07		Wesley																											
Topsoil spreading	5 days	Mon 5/14/07	Fri 5/18/07	109	Aldershot																											
Planting beds / sodding	10 days	Mon 5/21/07	Fri 6/1/07	110	Aldershot																											
Paving A gravel	7 days	Mon 6/4/07	Tue 6/12/07	111	Wesley																											
Paving	5 days	Wed 6/13/07	Tue 6/19/07	112	Wesley																											
Line painting	2 days	Wed 6/20/07	Thu 6/21/07	113	Wesley																											

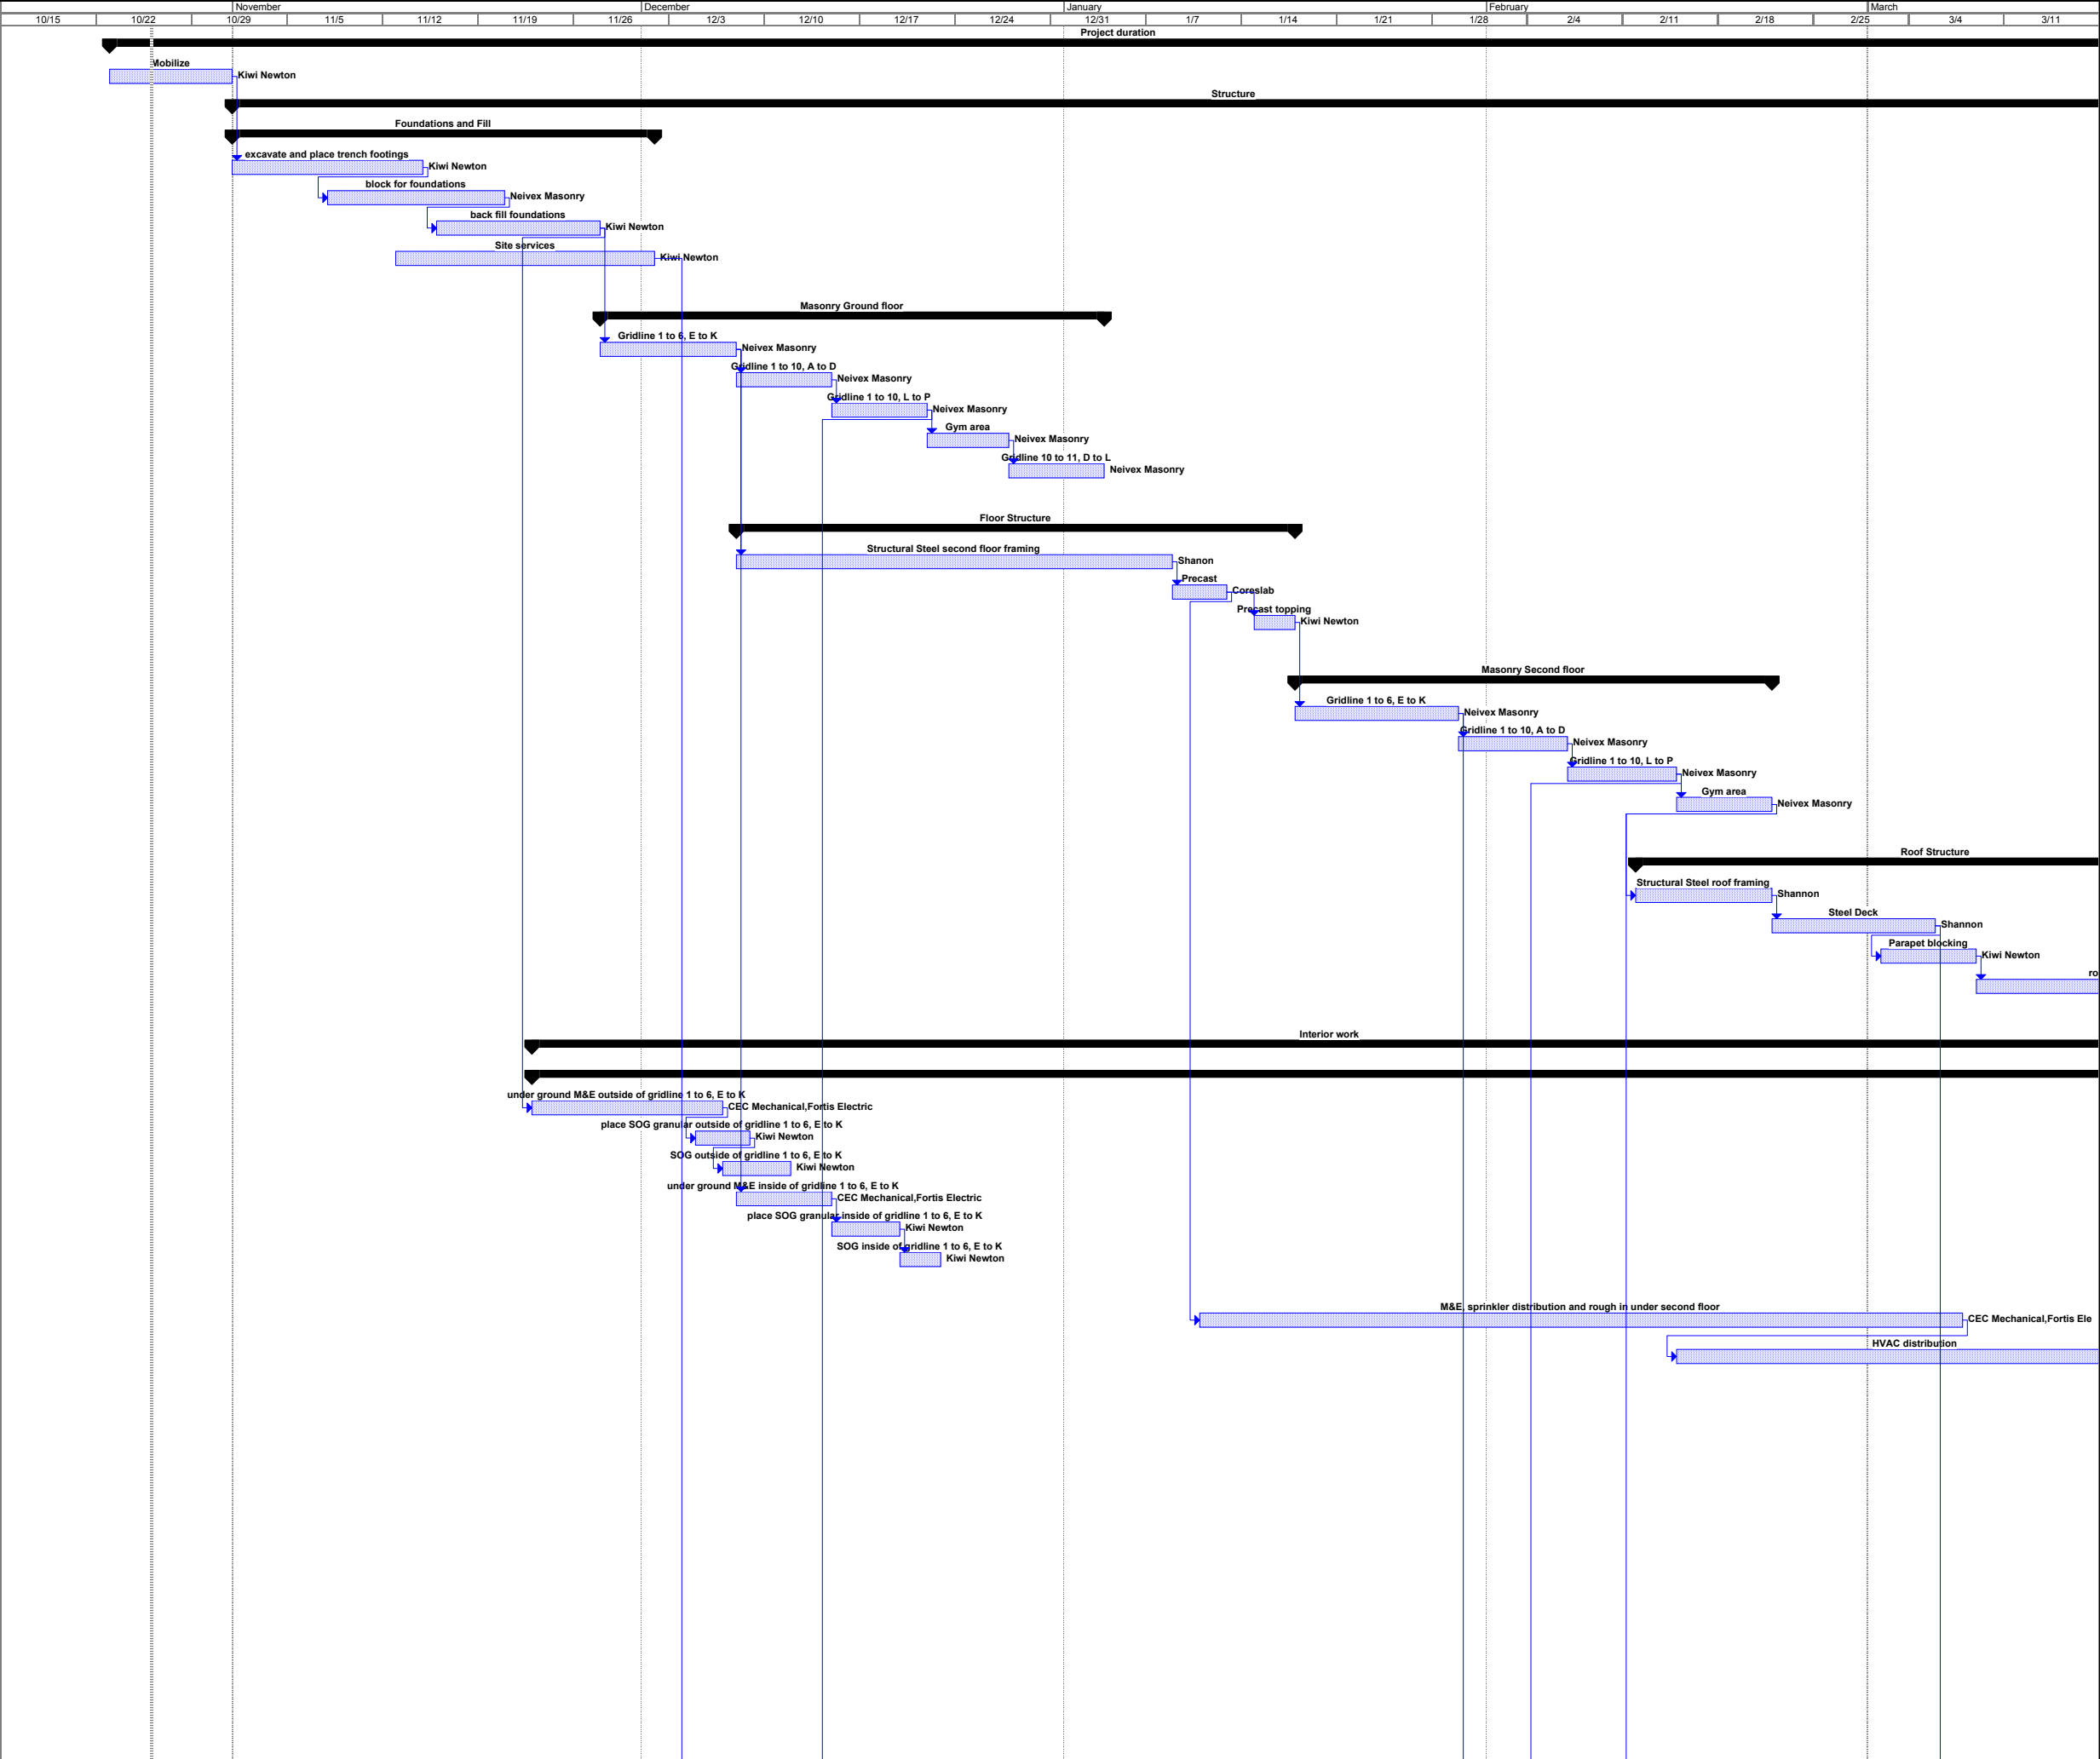
